

SERVICING REPORT GROUNDWATER SUMMARY

The form is to be completed by the Professional that prepared the Servicing Report.
 Use of the form by the City of Toronto is not to be construed as verification of engineering/hydrological content.

For City Staff Use Only:	
Name of ECS Case Manager (please print)	
Date Review Summary provided to to TW	

A. SITE INFORMATION	Included in SR (reference page number)	Report Includes this information City staff (Check)
Date Servicing Report was prepared: March 13/2020	Title	
Title of Servicing Report: Functional Servicing & Stormwater Management Report	Title	
Name of Consulting Firm that prepared Servicing Report: The Odan/Detech Group Inc.	Title	
Site Address 1507-1541 Avenue Rd.; 284-290 Lawrence Ave. W.	Title	
Postal Code	1	
Property Owner (identified on planning request for comments memo)	Title	
Proposed description of the project (ex. number of point towers, number of podiums, etc.)	1	
Land Use (ex. commercial, residential, mixed, industrial, institutional) as defined by the Planning Act	1	
Number of below grade levels	3	

SERVICING REPORT GROUNDWATER SUMMARY

<p>Does the SR include a private water drainage system (PWDS)?</p> <p>PWDS: Private Water Drainage System: A subsurface drainage system which may consist of but is not limited to weeping tile(s), foundation drain(s), private water collection sump(s), private water pump or any combination thereof for the disposal of private water on the surface of the ground or to a private sewer connection or drainage system for disposal in a municipal sewer.</p>	<p>If Yes continue completing Section B (Information Relating to Groundwater) <u>ONLY</u></p> <p>If Yes, Number of PWDS? _____ 1 _____</p> <p><i>(Each of these PWDS may require a separate Toronto Water agreement)</i></p> <p>If No skip to Sections C (On-site Groundwater Containment) and/or D (Water Tight Requirements) as applicable</p>	<p><input checked="" type="radio"/> YES</p> <p><input type="radio"/> NO</p>	
B. INFORMATION RELATING TO GROUNDWATER		Included in SR (reference page number)	Report Includes this information City Staff (Check)
<p>A copy of the pump schedule(s) for ALL groundwater sump pump(s) for the development site has been included in the FSR</p> <p style="text-align: center;"><u>or</u></p> <p>A letter written by a Mechanical Consultant (signed and stamped by a Professional Engineer of Ontario) shall be attached to the SR stating the peak flow rate of the groundwater discharge for the development site for all groundwater sump pump(s). This peak flow rate must be based on the pump schedule(s) that have been designed by the Mechanical Consultant. A template of this letter is attached in Schedule A.</p>	<p>In the absence of a mechanical pump flow rate letter, a conservative flow rate has been assumed for each of the two PWDS. We understand that if this flow rate requires revision in the future, the report may require revision and reapproval.</p>	36	

SERVICING REPORT GROUNDWATER SUMMARY

<p>**If there is more than one sump they must ALL be included in the letters along with a combined flow**</p>			
<p>Is it proposed that the groundwater from the development site will be discharged to the sanitary, combined or storm sewer?</p>	<p>Yes Sanitary Sewer</p> <p><input type="radio"/> Combined Sewer</p> <p><input type="radio"/> Storm Sewer</p>	9	
<p>Will the proposed PWDS discharge from the site go to the Western Beaches Tunnel (WBT)?</p> <p>*Reference attached WBT drainage map*</p>	<p><input type="radio"/> YES <input type="radio"/> NO</p> <p style="text-align: center;">No</p> <p>If Yes, private water discharge fees will apply and site requires a sanitary discharge agreement.</p>		
<p>What is the street name where the receiving sewer is located?</p>	<p>Avenue Rd.</p>	9	
<p>What is the diameter of the receiving sewer?</p>	<p>300mm</p>	9	
<p>Is there capacity in the proposed local sewer system?</p> <p>YES <input type="radio"/> NO</p>	<p>Are there any improvements required to the sewer system? If yes, identify them below and refer to the section and page number of the FSR where this information can be found.</p> <p>If a sewer upgrade is required, the owner is required to enter into an Agreement with the City to improve the infrastructure?</p> <p style="text-align: right;"><input type="radio"/> YES</p>	12, 13	
<p>Total allowable peak flow rate during a 100 year storm event (L/sec) to storm sewer</p> <p>When groundwater is to be discharged to the storm sewer the total groundwater and stormwater discharge shall not exceed the permissible peak flow rate during a 2 year pre development storm event, as per the City's</p>	<p>_ 133.6 ___ L/sec</p>	16	

SERVICING REPORT GROUNDWATER SUMMARY

Wet Weather Flow Management Guidelines, dated 2006			
<p>Short-Term Groundwater Discharge Provide proposed total flow rate to the sanitary/combined sewer in post-development scenario</p> <p>Total Flow (L/sec) = sanitary flow + peak short-term groundwater flow rate</p>	<p>5.4 _____ L/sec</p>	36	
<p>Long-Term Groundwater Discharge Provide proposed total flow rate to the sanitary/combined sewer in post-development scenario</p> <p>Total Flow (L/sec) = sanitary flow + peak long-term groundwater flow rate</p>	<p>1.3 L/s GW + 7.11 + 11.31L/s SAN + 0.29 L/ s I/I = 20.01L/s _____ L/sec</p>	9	
<p>Does the water quality meet the receiving sewer Bylaw limits?</p> <p><input checked="" type="radio"/> YES</p> <p><input type="radio"/> NO</p>	<p>If the water quality does not meet the applicable receiving sewer Bylaw limits and the applicant is proposing a treatment system the applicant will need to include a letter stating that a treatment system will be installed and the details of the treatment system will be included in the private water discharge application that will be submitted to TW EM&P.</p>		
<p>C. ON-SITE GROUNDWATER CONTAINMENT</p> <p style="font-size: 1.2em; margin-top: 20px;">NOT APPLICABLE</p>		<p>Included in SR (reference page number)</p>	<p>Report Includes this information City Staff (Check)</p>
How is the site proposing to manage the groundwater discharge on site?			

SERVICING REPORT GROUNDWATER SUMMARY

<p>Has the above proposal been approved by:</p>	<p><input type="radio"/> TW-WIM And <input type="radio"/> TW-EM&P And <input type="radio"/> ECS NOT APPLICABLE</p>		
<p>If the site is proposing a groundwater infiltration gallery, has it been stated that the groundwater infiltration gallery will not be connected to the municipal sewer? A connection between the infiltration gallery/dry well and the municipal sewer is not permitted</p> <p>Please be advised if an infiltration gallery/dry well on site is not connected to the municipal sewer, the site must submit two letters using the templates in Schedule B and Schedule C.</p>	<p><input type="radio"/> YES <input type="radio"/> NO NOT APPLICABLE</p>		
<p>Confirm that the infiltration gallery can infiltrate 100% of the expected peak groundwater flow year round, ensure that the top of the infiltration trench is below the frost line (1.8m depth), not less than 5 m from the building foundation, bottom of the trench 1m above the seasonally high water table, and located so that the drainage is away from the building.</p>	<p>NOT APPLICABLE</p>		
<p>D. WATER TIGHT REQUIREMENTS</p> <p>NOT APPLICABLE</p>		<p>Included in SR (reference page number)</p>	<p>Report Includes this information City Staff</p>

October 2017

SERVICING REPORT GROUNDWATER SUMMARY


		(Check)
If the site is proposing a water tight structure: 1. The owner must submit a letter using the template in Schedule D. 2. A Professional Engineer (Structural), licensed to practice in Ontario and qualified in the subject must submit a letter using the template in Schedule E.	NOT APPLICABLE	

Provide a copy of the approved SR to Toronto Water Environmental Monitoring & Protection Unit at pwapplication@toronto.ca.

Consulting Firm that prepared Servicing Report: The Odan/Detech Group Inc.

Professional Engineer who completed the report summary: Daniel Bancroft, P.Eng.
Print Name

Professional Engineer who completed the report summary: _____
Signature

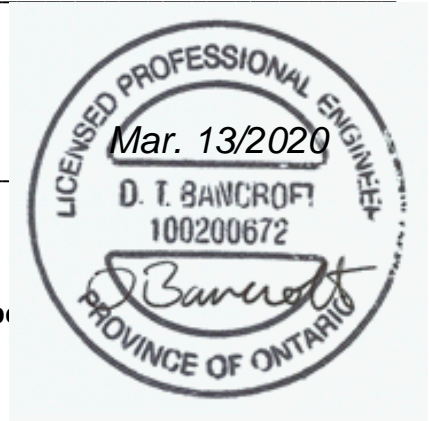

Schedule A: Template Letter from Mechanical Consultant confirming p

- [Mechanical Consultant Company Letterhead]
- [Company Name]
- [Company Address and Contact Information]

[Date]

Attention: Executive Director, Engineering and Construction Services
 c/o Manager, Development Engineering

[ADDRESS]

cc: General Manager, Toronto Water
 c/o Manager, Environmental Monitoring and Protection Unit
 30 Dee Ave, Toronto ON M9N 1S9
